

# FORTNIGHTLY UPDATE 07.10.2022

## SAINT IGNATIUS COLLEGE | MACKILLOP SENIOR CENTRE

Plan Group are proud to present our second fortnightly update for the Saint Ignatius College Mackillop Senior Centre!

Welcome back to term 4!

Since our last update, we have been very busy getting as much construction works completed during the school holiday break as we can. This includes ongoing excavation of footings, and lift pit works in preparation for our southern ground floor slab pour. Off-site, we have made significant inroads with our steel and precast detailing, as well as the continuation of project planning, materials procurement, and task scheduling.


We are very much looking forward to getting some concrete in the ground, to aid in our protection from recent and upcoming wet weather.

### COMPLETED TASKS

- Southern footing excavation & blinding concrete
- Preparation for pouring lift pit
- North-west retaining wall construction
- Steel and precast panel detailing

### UPCOMING TASKS

- In-ground services installation
- Pour lift pit walls
- Footing excavation remaining ongoing
- Pour southern GF slab
- Manufacture of precast panels

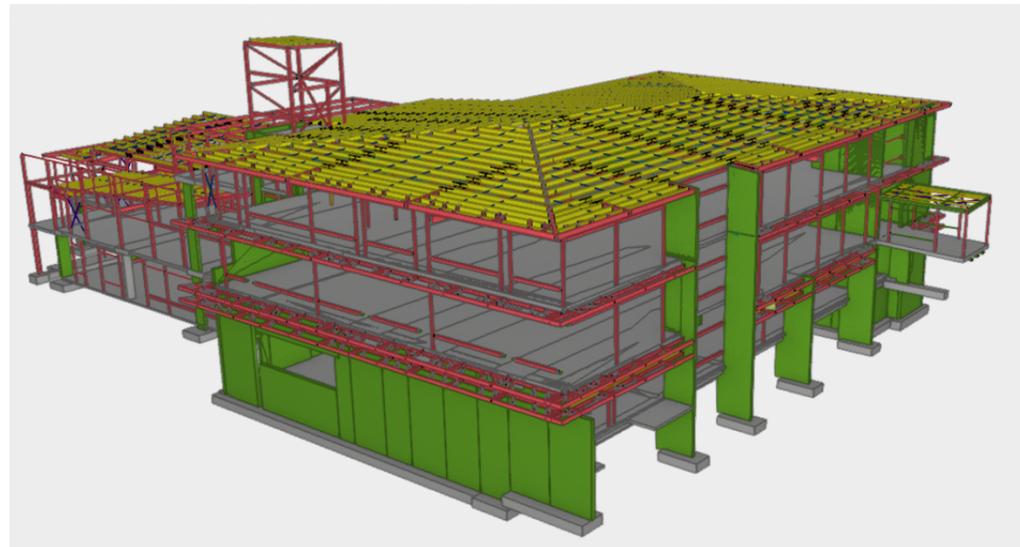

### YOUR PROJECT TEAM



**Alex Simpson**  
Project Manager



**Paul Hunt**  
Site Manager



**Adam McPhee**  
Site Foreman



**Jacob Bunn**  
Contract Administrator

For further enquiries, please email our project team below;  
STIGS@PLANGROUP.COM.AU

